STATE OF OREGON
MONITORING WELL REPORT
(as required by ORS 537.765 & OAR 690-240-095)

WASH 56200

Well ID# L38478

Start Card # 130050

Instructions for completing this report are on the last page of this form.

(1) OWNER/PROJECT: WELL NO. DMW-14B

Name Nimbus Oaks LLC

Address 111 SW Columbia

City Portland State OR Zip 97201

(2) TYPE OF WORK:

[X] New construction [ ] Alteration (Repair/Recondition)
[ ] Conversion [ ] Deepening [ ] Abandonment

(3) DRILLING METHOD

[X] Rotary Air [ ] Rotary Mud [ ] Cable
[ ] Hollow Stem Auger [ ] Other

(4) BORE HOLE CONSTRUCTION

Special Standards Yes [X] No [ ] Depth of completed well 145 ft.

Land surface

Vault 0 ft. TO 1 ft.

Seal 1 ft. TO 131 ft.

133'-131' 20x40 Sand

Filter pack 133 ft. TO 146 ft.

Water-tight cover
Surface flush vault
Locking cap

Casing diameter 2 in.
material PVC Sch 80
Welded [ ] Threaded [X] Glued [ ]

Liner diameter ___ in.
material N/A
Welded [ ] Threaded [ ] Glued [ ]

Well seal:
Material AQUA Gard
Amount 32 lbs
Grout weight 9.5
Borehole diameter 8.0 in.

Bentonite plug at least 3 ft. thick

Screen material PVC Sch 80
interval(s):
From 145 To 135
From ___ To ___
Slot size .020 in.

Filter pack:
Material Silica Sand
Size 10x20 in.

(5) WELL TEST:

[ ] Pump [ ] Bailer [ ] Air [ ] Flowing Artesian

Permeability ___ Yield ___ GPM

Conductivity ___ pH ___

Temperature of water 56 °F/C Depth artesian flow ___

Was water analysis done? [ ] Yes [ ] No

By whom? ___

Depth of strata to be analyzed. From ___ ft. to ___

Remarks: ___

Name of supervising Geologist/Engineer ___

RECEIVED JUL 19 2000 WATER RESOURCES DEPT. SALEM, OREGON

(6) LOCATION OF WELL By legal description

Well Location: County Washington

Township 1S (N or S) Range 1W (E or W) Section 27

1. NE 1/4 of SE 1/4 of above section.

2. Either Street address of well location Beaverton, OR 9100 SW Nimbus Drive

or Tax lot number of well location 400

3. ATTACH MAP WITH LOCATION IDENTIFIED. Map shall include approximate scale and north arrow.

(7) STATIC WATER LEVEL:

18 Ft. below land surface. Date ___

Artesian Pressure ___ lb/sq. in. Date ___

(8) WATER BEARING ZONES:

Depth at which water was first found ___

From	To	Est. Flow Rate	SWL
18	146	8-20 GPM	

(9) WELL LOG: Ground elevation ___

Material	From	To	SWL
Sandy Gravel	0	21	
Basalt Gray	21	149	18
14"OD: 0-21'			
12" : 21-26'			
10.5" : 26- 102'			
8.5" : 102-149			
Bentonite 149-146			

RECEIVED OCT 30 2000 WATER RESOURCES DEPT SALEM, OREGON

Date started 6-11-00 Completed 6-12-00

(unbonded) Monitor Well Constructor Certification:

I certify that the work I performed on the construction, alteration, or abandonment of this well is in compliance with Oregon well construction standards. Materials used and information reported above are true to the best knowledge and belief.

MWC Number 10464

Signed ___ Date 7-10-00

(bonded) Monitor Well Constructor Certification:

I accept responsibility for the construction, alteration, or abandonment work performed on this well during the construction dates reported above. All work performed during this time is in compliance with Oregon well construction standards. This report is true to the best of my knowledge and belief.

MWC Number 10024

Signed ___ Date 7/17/00

OR0112 ORIGINAL & FIRST COPY-WATER RESOURCES DEPARTMENT SECOND COPY-CONSTRUCTOR THIRD COPY-CUSTOMER

GAF/Phase II Work Plan | T:\530\001\015\FIGA.DWG (A) 4/10/2000

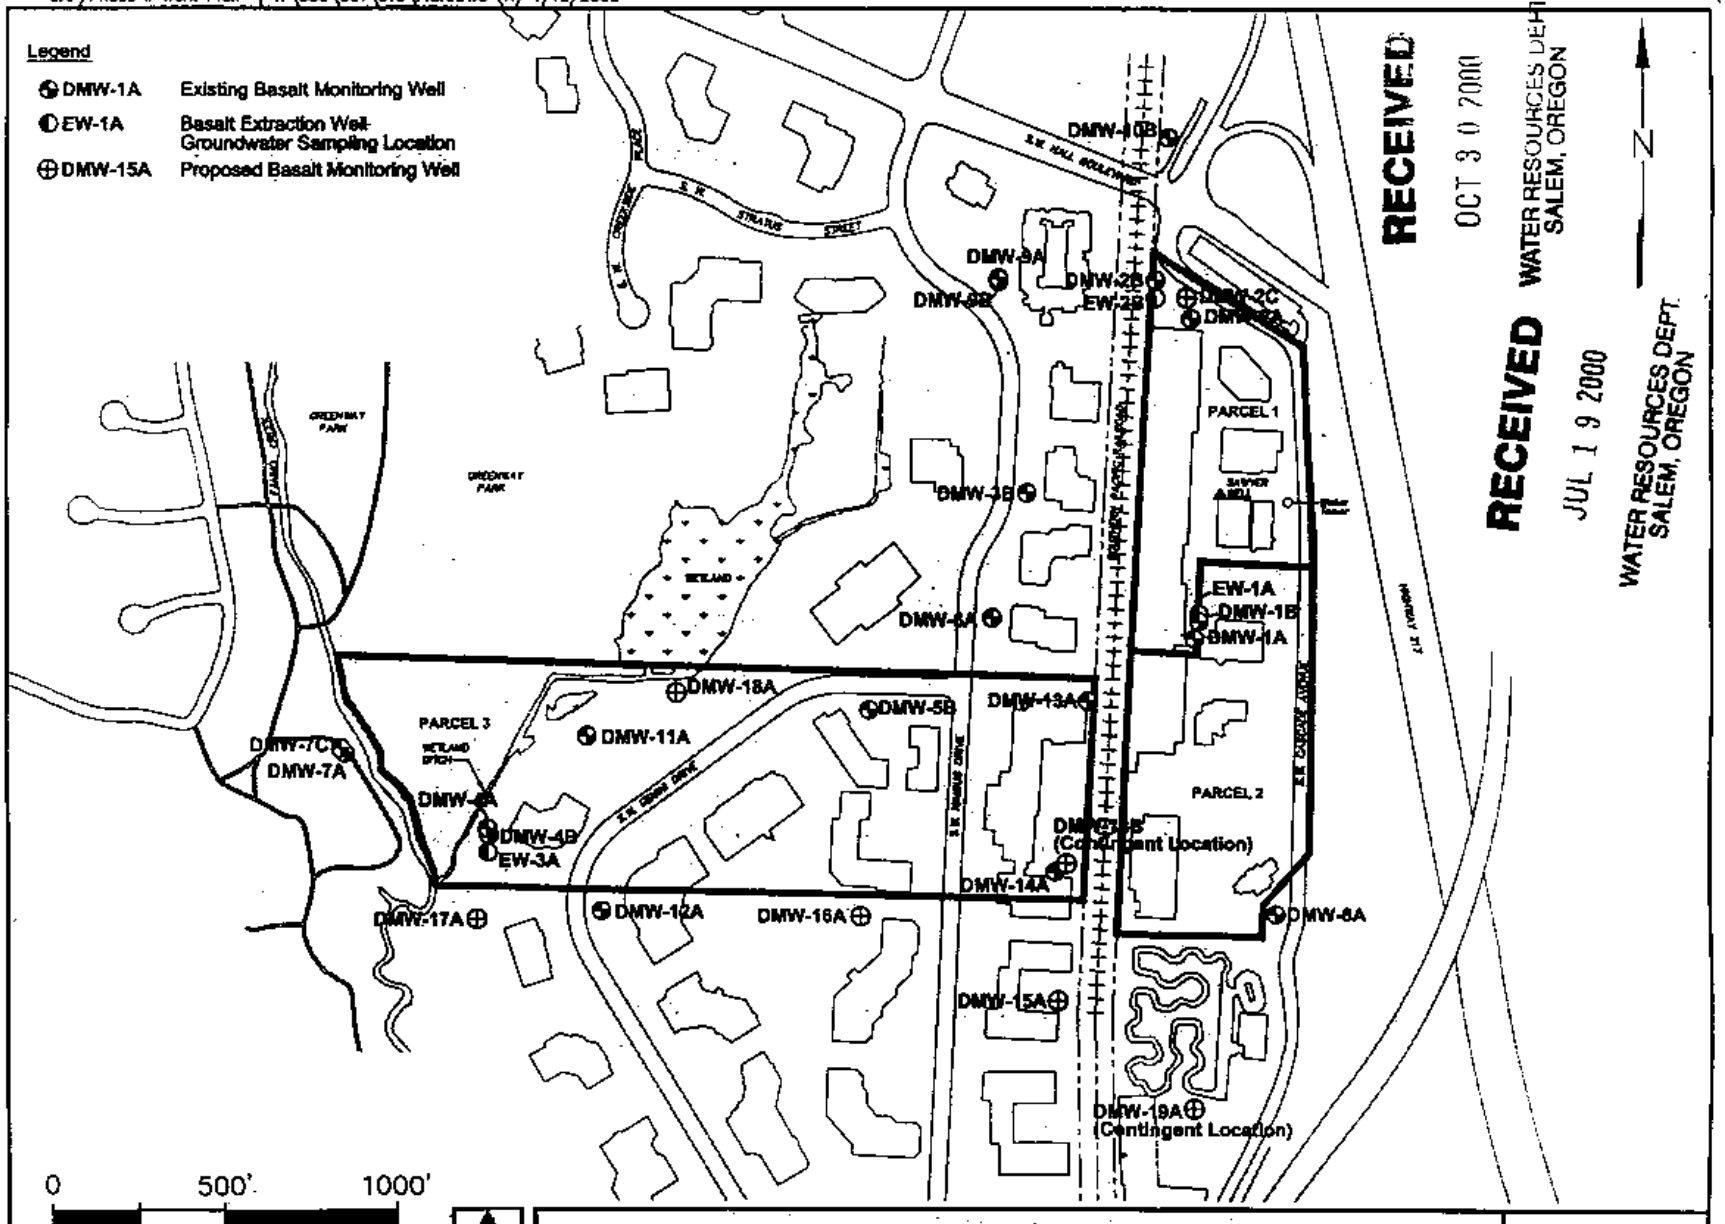

Existing and Proposed CRBG Monitoring and Extraction Wells

Figure 2-3

RECEIVED
OCT 30 2000
WATER RESOURCES DEPT
SALEM, OREGON
RECEIVED
JUL 19 2000
WATER RESOURCES DEPT.
SALEM, OREGON
