STATE OF OREGON

MONITORING WELL REPORT

(as required by ORS 537.765 & OAR 690-240-095)

WASH 55999

Well ID# L38469

Start Card # 130044

Instructions for completing this report are on the last page of this form.

(1) OWNER/PROJECT: WELL NO. DMW-17A

Name PS Business Parks LP Dept: PT

Address PO BOX 125025 ORD3090

City Glendale State CA Zip 91201

(2) TYPE OF WORK:

☒ New construction ☐ Alteration (Repair/Reconditioning)

☐ Conversion ☐ Deepening ☐ Abandonment

RECEIVED JUN 08 2000 WATER RESOURCES DEPT SALEM, OREGON

(3) DRILLING METHOD

☒ Rotary Air ☐ Rotary Mud ☐ Cable

☐ Hollow Stem Auger ☐ Other

(4) BORE HOLE CONSTRUCTION

Special Standards Yes ☒ No ☐ Depth of completed well 80' 100' ft.

Land surface

Vault 0 ft. TO 3' ft.

Seal 3' ft. TO 60' ft.

20x40 Sand 62'-60' Filter pack

62' ft. TO 81' ft.

Water-tight cover

Surface flush vault

Locking cap

Casing diameter 2" in.

material

Welded ☐ Threaded ☒ Glued ☐

Liner diameter in.

material N/A

Welded ☐ Threaded ☐ Glued ☐

Well seal:

Material 30% Volclay Grout

Amount 45, 50 lbs Bags

Grout weight 9.5

Borehole diameter 8.5 in.

Bentonite plug at least 3 ft. thick

Screen material PVC Sch 80

interval(s): From 80' To 65'

From To

Slot size 020 in.

Filter pack:

Material Silica Sand

Size 10X20 in.

(5) WELL TEST:

☐ Pump ☐ Bailer ☐ Air ☐ Flowing Artesian

Permeability Yield GPM

Conductivity PH

Temperature of water 56° °F/C Depth artesian flow found ft.

Was water analysis done? ☐ Yes ☐ No

By whom?

Depth of strata to be analyzed. From ft. to ft.

Remarks:

Name of supervising Geologist/Engineer

(6) LOCATION OF WELL By legal description

Well Location: County Washington

Township 1S (N or S) Range 1W (E or W) Section 27

1. NW 1/4 of SE 1/4 of above section.

2. Either Street address of well location 9205 SW Gemini Dr. Beaverton, OR

or Tax lot number of well location 500

3. ATTACH MAP WITH LOCATION IDENTIFIED. Map shall include approximate scale and north arrow.

(7) STATIC WATER LEVEL:

1' Ft. below land surface. Date 5-18-00

Artesian Pressure lb/sq. in. Date

(8) WATER BEARING ZONES:

Depth at which water was first found 28'

From	To	Est. Flow Rate	SWL
28'	65'	3 GPM	
65'	100'	8 GPM	1'

(9) WELL LOG: Ground elevation

Material	From	To	SWL
Gray silty sand	0	12'	1'
Weathered Basalt	12'	15'	
Basalt	15'	65'	
Weathered Basalt	65'	80'	
Black Basalt	80'	100'	
(*) Back Fill hole with 3/8 Bentonite Chips.	100'-81'		
Hole size: 0-14'	12"		
14'-24'	10 1/4"		
24-100	8 3/4"		

Date started 5-17-00 Completed 5-18-00

(unbonded) Monitor Well Constructor Certification:

I certify that the work I performed on the construction, alteration, or abandonment of this well is in compliance with Oregon well construction standards. Materials used and information reported above are true to the best knowledge and belief.

MWC Number 10464

Signed Date 5-18-00

(bonded) Monitor Well Constructor Certification:

I accept responsibility for the construction, alteration, or abandonment work performed on this well during the construction dates reported above. All work performed during this time is in compliance with Oregon well construction standards. This report is true to the best of my knowledge and belief.

MWC Number 10024

Signed Date 6/6/00

ORD112 ORIGINAL & FIRST COPY-WATER RESOURCES DEPARTMENT SECOND COPY-CONSTRUCTOR THIRD COPY-CUSTOMER

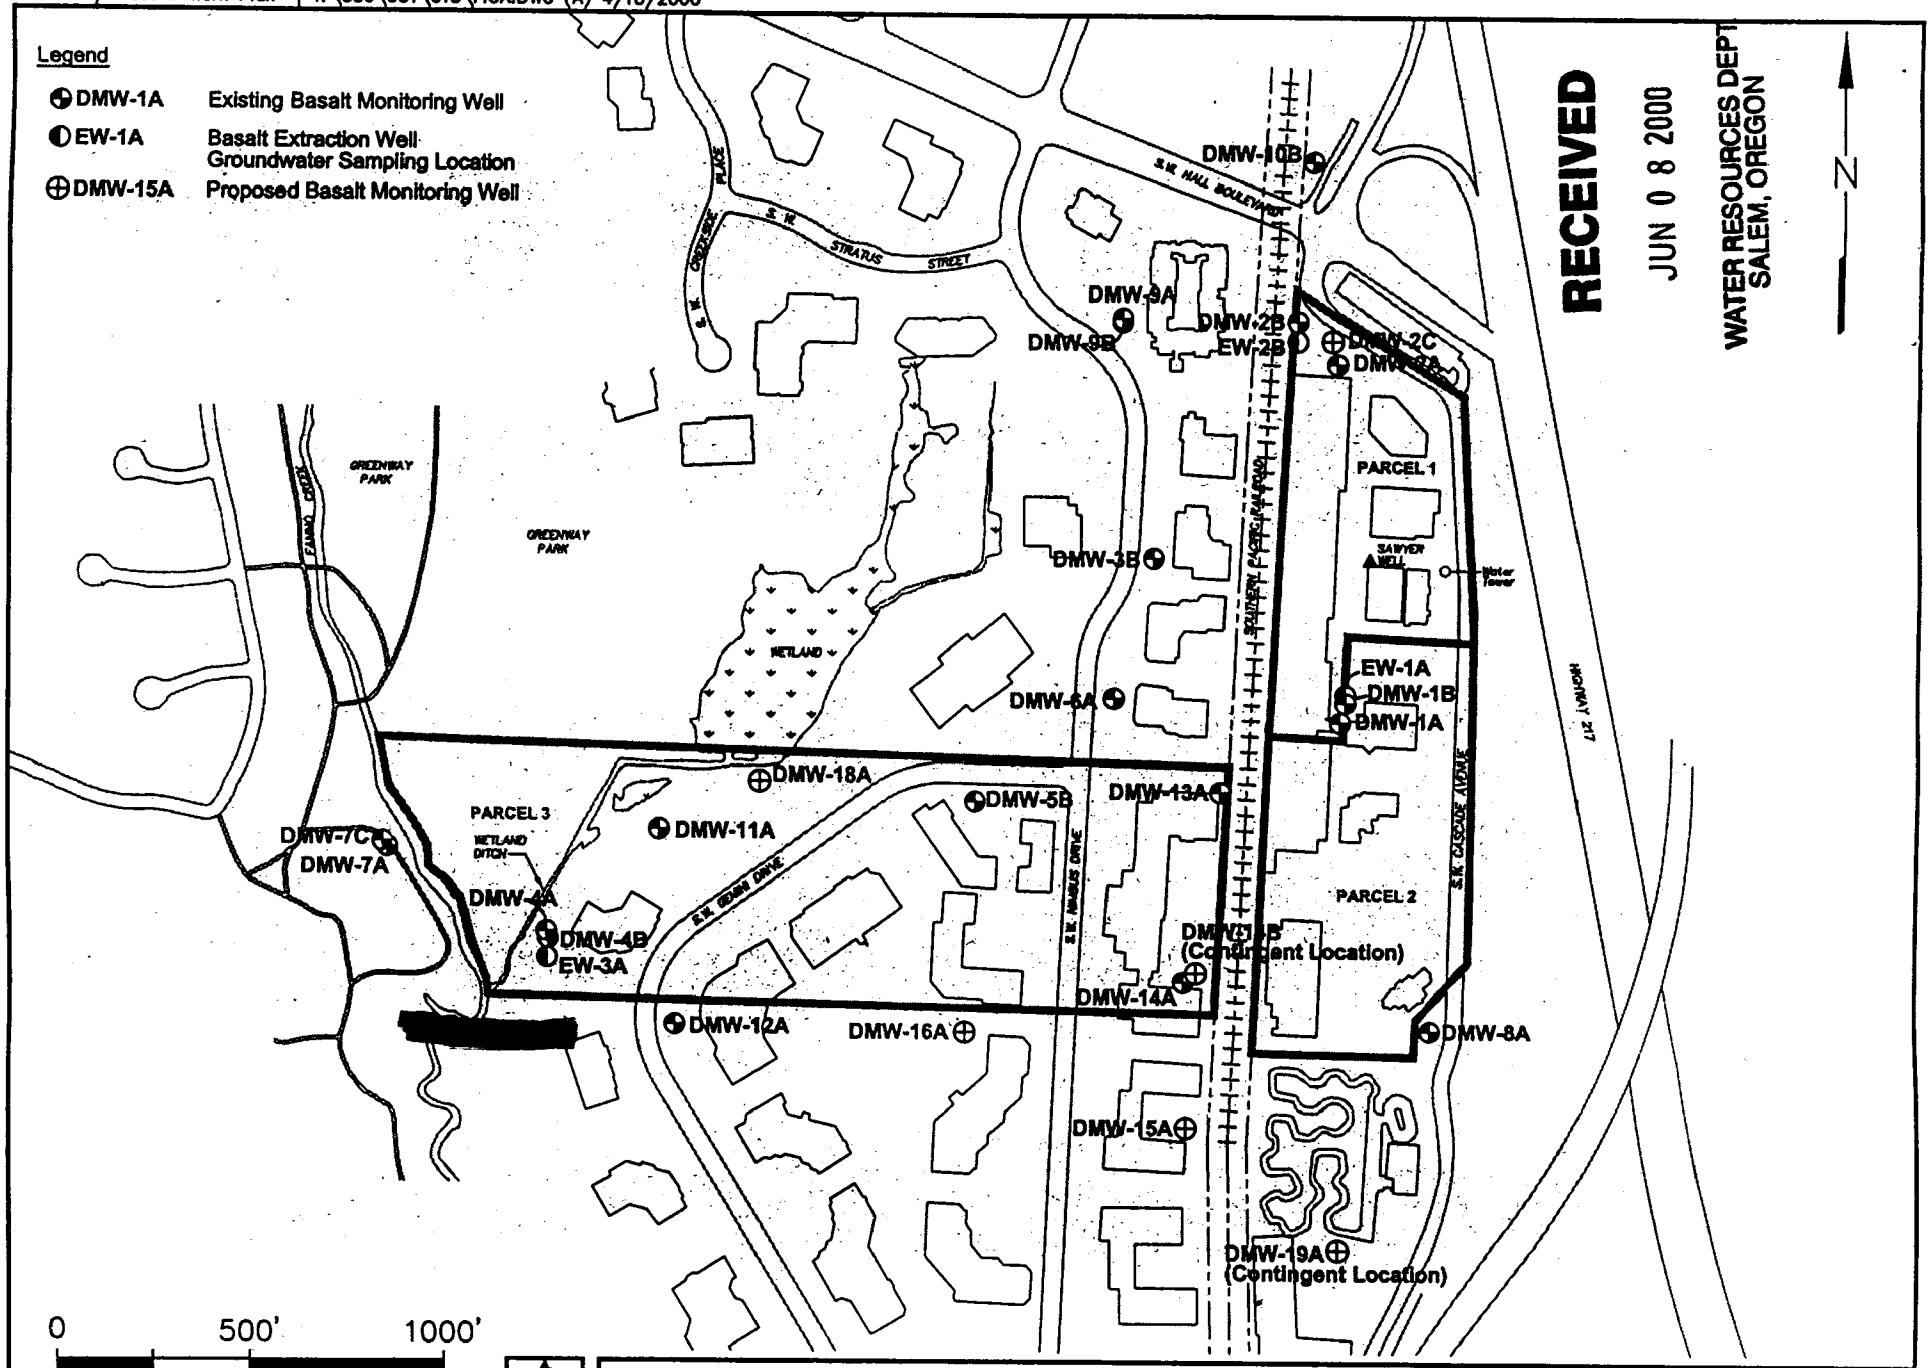

Existing and Proposed CRBG Monitoring and Extraction Wells

Figure 2–3

RECEIVED
JUN 0 8 2000
WATER RESOURCES DEPT
SALEM, OREGON
